










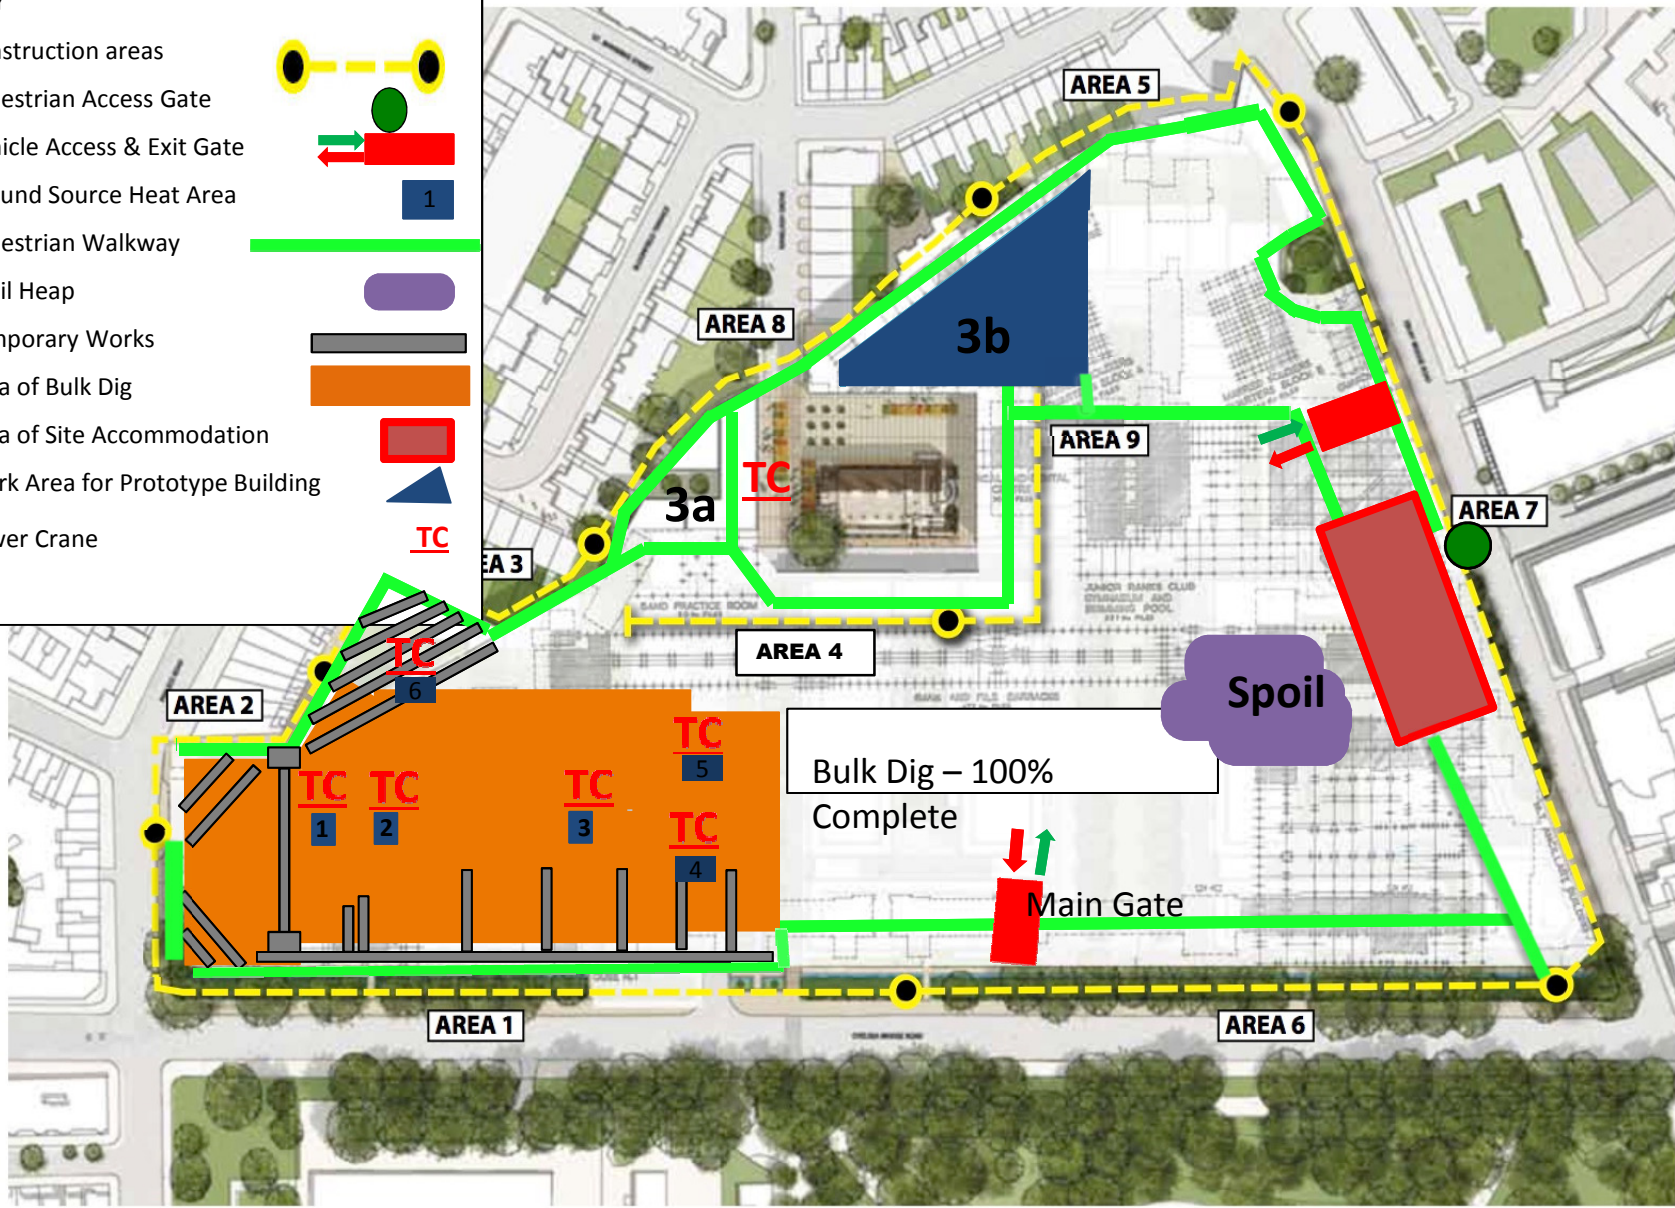


KEY

- Construction areas 
- Pedestrian Access Gate 
- Vehicle Access & Exit Gate 
- Ground Source Heat Area 
- Pedestrian Walkway 
- Spoil Heap 
- Temporary Works 
- Area of Bulk Dig 
- Area of Site Accommodation 
- Work Area for Prototype Building 
- Tower Crane 





Site Works – WC 22/02/2016

Area Ref	Area	Short Term	Status	Long Term
1 2	Area 1	<p>Substructure and Superstructure works underway. Area 2 temporary works commenced.</p> <p>Jump form commencing on Core 1/Block 1 and climbing.</p> <p>New crane (TC6) to be erected 15/02/16.</p> <p>TC1 (down 21/06/16).</p> <p>TC2 (down 26/07/16).</p> <p>TC3 (down 15/07/16).</p> <p>TC4 (down 04/08/16).</p> <p>TC6 (down TBC)</p>	<p>Ongoing</p> <p>Ongoing</p>	
3a	Northern Boundary Wall and Area 3a	<p>Concrete re-structure commenced.</p> <p>Pouring concrete.</p> <p>Crane down 28/02/16..</p> <p>Waterproofing temp work.</p> <p>Casting Columns.</p> <p>First Floor Slabs Commenced.</p> <p>Drainage installed Ranelagh Grove.</p>	<p>Ongoing</p> <p>Ongoing</p> <p>Ongoing</p> <p>Ongoing</p> <p>Ongoing</p> <p>Ongoing</p>	
4	Vehicle access and ramp	<p>Vehicles in and out of area.</p> <p>TC5 (down 15/08/16).</p>	Ongoing	
5	Northern Boundary Wall	<p>Draining heading works on Ranelagh Grove.</p> <p>Erection of internal hoardings for Temporary Prototype Building.</p>	Ongoing	
6	Chelsea Bridge Road	<p>Traffic Marshals on both side of the road to make pedestrians and cyclists are safe.</p> <p>Gas mains installation complete.</p> <p>Installation of silt-buster water treatment system.</p>	Complete	



Site Works – WC 22/02/2016

Area Ref	Area	Short Term	Status	Long Term
7	Ebury Bridge Road	<p>Improvements made to on site drainage and waste water usage for wheel washing.</p> <p>Gate barrier erected on Ebury Bridge road close to pavement.</p>	<p>Completed</p> <p>Completed</p>	
8 3b	Northern Boundary Wall and Area 3b	<p>Prototype building works. Roof works.</p> <p>Area lighting reassessed to reduce light pollution for near neighbours.</p> <p>Ground works and external finishes.</p>	<p>Ongoing</p> <p>Completed.</p> <p>Ongoing</p>	Target completion date April 2016.
Site Wide	Outside of Site	<p>SES (<i>Site Engineering Surveys</i>)</p> <p>Surveying to Levelling Point.</p>		Survey to levelling points.
