


- KEY**
- Construction areas
 - Pedestrian Access Gate
 - Vehicle Access & Exit Gate
 - Ground Source Heat Area
 - Pedestrian Walkway
 - Spoil Heap
 - Temporary Works
 - Area of Bulk Dig
 - Area of Site Accommodation
 - Work Area for Prototype Building
 - Tower Crane
 - Jump form core



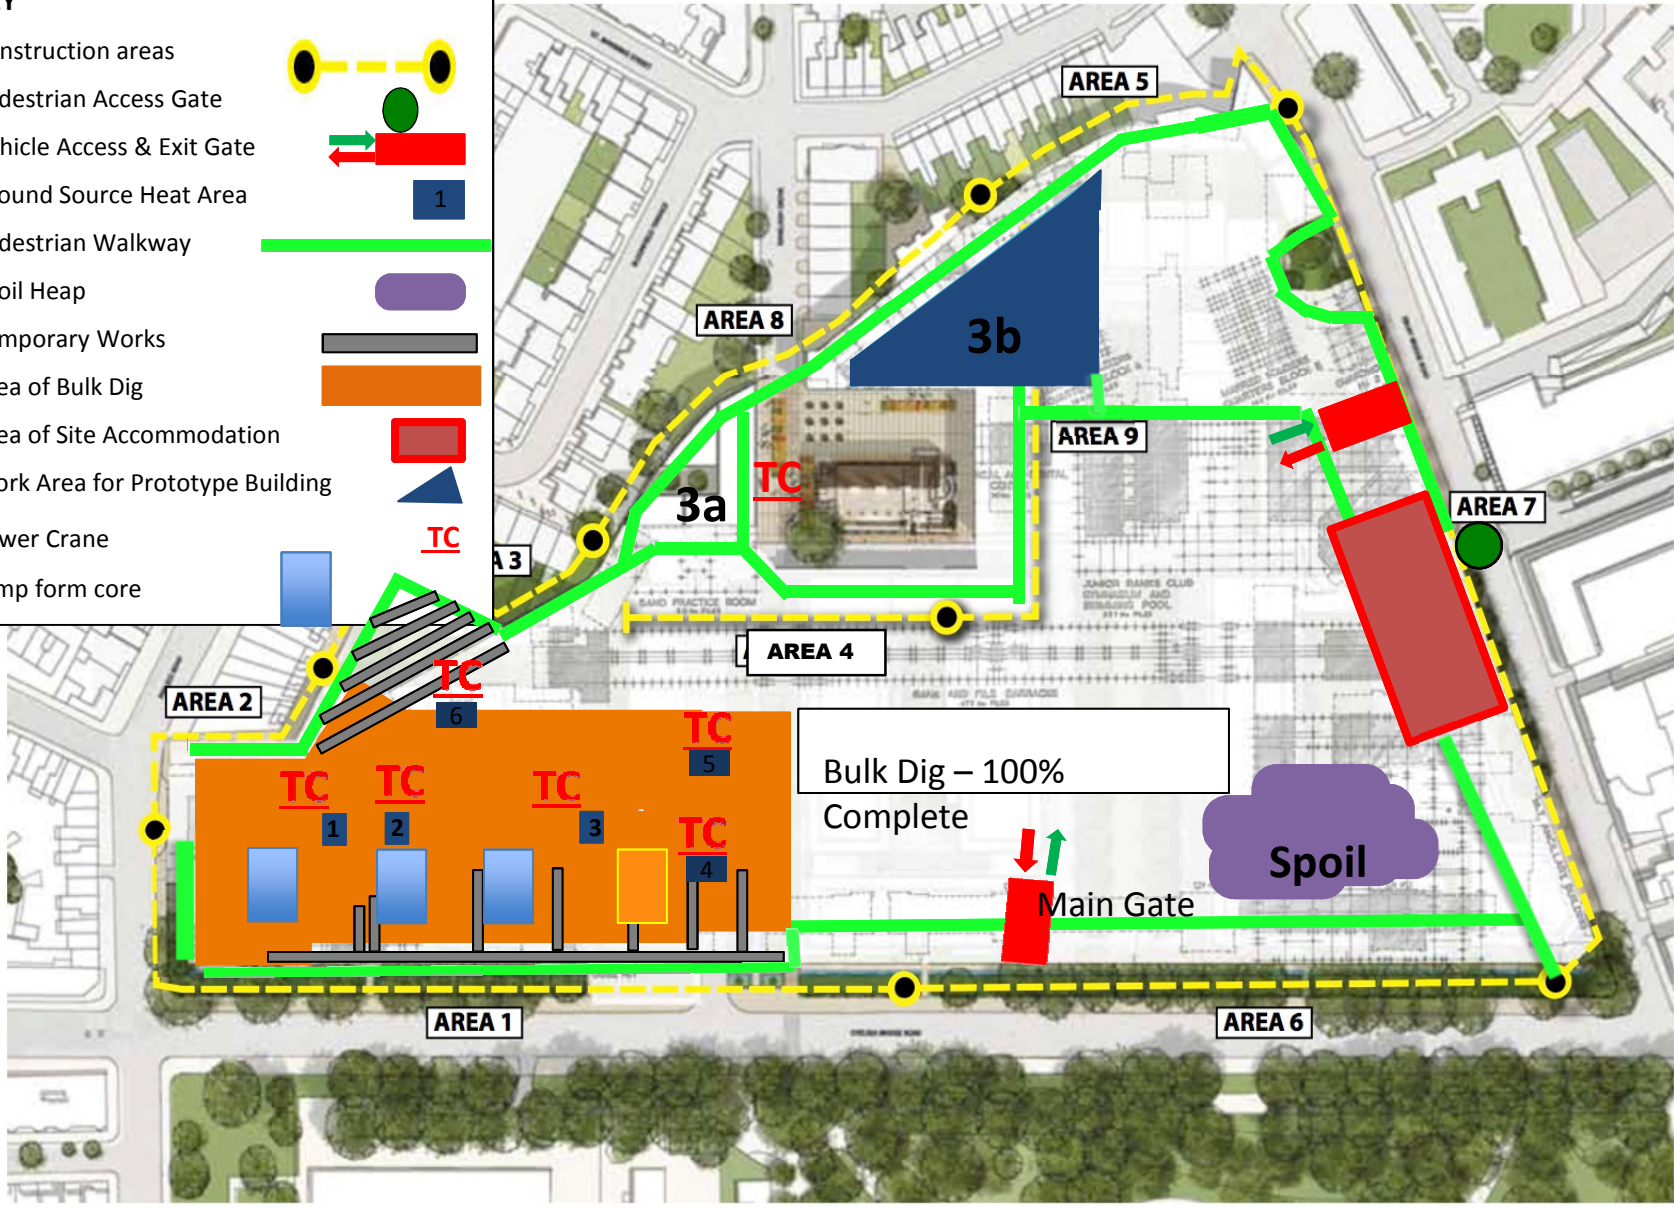

Site Works – WC 09/05/2016

Area Ref	Area	Short Term	Status	Long Term
1 2	Area 1	<ul style="list-style-type: none"> Substructure and Superstructure works underway. Jump forms underway on cores 1, 2, 3, one being the highest up to date. Drainage continues to be installed. TC1 (down 21/06/16). TC2 (down 26/07/16). TC3 (down 15/07/16). TC4 (down 04/08/16). TC6 (down 08/16)	Ongoing Ongoing Ongoing	Continuing to follow the core up until completion. Jump forms will continue with a weekly cycle.
3a	Northern Boundary Wall and Area 3a	<ul style="list-style-type: none"> Striking of false work in 3A Erecting of scaffolding around structure Construction of access scaffolding and hoist. Installation of new access gate. Completion of new paved area. 	Ongoing Ongoing Ongoing Ongoing Ongoing	Handover and opening of the new marketing suite. Brickwork to begin on 3A
	Vehicle access and ramp	Vehicles in and out of area. TC5 (down 15/08/16).	Ongoing	
4 5	Northern Boundary Wall Chelsea Bridge Road	Draining heading works on Ranelagh Grove. Erection of internal hoardings for Temporary Prototype Building. Traffic Marshals on both side of the road to make pedestrians and cyclists are safe. Gas mains installation complete.	Ongoing	
6		Installation of silt-buster water treatment system.	Complete	



Site Works – WC 09/05/2016

Area Ref	Area	Short Term	Status	Long Term
7	Ebury Bridge Road	<p>Improvements made to on site drainage and waste water usage for wheel washing.</p> <p>Gate barrier erected on Ebury Bridge road close to pavement.</p>	<p>Completed</p> <p>Completed</p>	
8 3b	Northern Boundary Wall and Area 3b	<p>Prototype building works. Roof works.</p> <p>Area lighting reassessed to reduce light pollution for near neighbours.</p> <p>Ground works and external finishes.</p>	<p>Ongoing</p> <p>Completed.</p> <p>Ongoing</p>	Target completion date April 2016.
Site Wide	Outside of Site	<p>SES (<i>Site Engineering Surveys</i>)</p> <p>Surveying to Levelling Point.</p>		Survey to levelling points.
